

Notice to Mariners No 27 / 2017
Blyth Offshore Demonstrator Project
10th October 2017

BOD-101-04-SMC-NTM-00045-A-01

Construction Update

Gravity Base Foundations (GBFs).

Please note - All mariners are requested to maintain a minimum 500m safety zone around each turbine location indicated in Chart 1 and Table 1.

Chart 1 - Array 2 Site and Turbine/GBF Locations

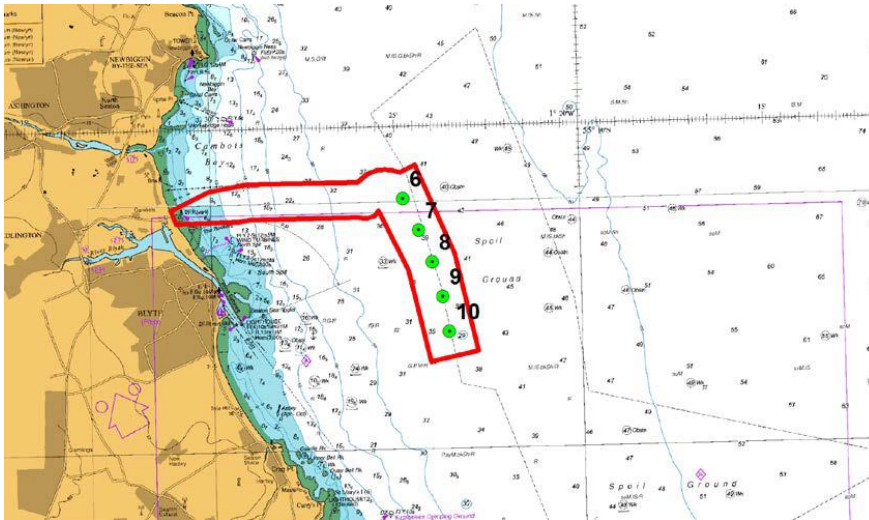


Table 1 - Turbine Placement Locations

Location	Position	
GBF Location 6	N55°08.8702'	W001°24.7913'
GBF Location 7	N55°08.3793'	W001°24.3781'
GBF Location 8	N55°07.8805'	W001°24.0344'
GBF Location 9	N55°07.3406'	W001°23.7706'
GBF Location 10	N55°06.7974'	W001°23.6067'

Activity 1: GBF Post-installation Works & Commissioning


Please be advised that GBF post-installation works will be continuing on the BOD Project Array 2 site.

The vessel *Nordnes* will return to site to complete scour protection rock player around the GBF locations. The vessel is expected onsite 11th October for approximately 1-3 days (weather depending).

Notice to Mariners No 27 / 2017
Blyth Offshore Demonstrator Project
10th October 2017

BOD-101-04-SMC-NTM-00045-A-01

Vessel details:

Name	Nordnes - flexible fallpipe vessel	
Operator	Van Oord	
IMO	9229910	
Call sign	PHOG	
Masters	Kees van Dalen, Eelco Laurens Roos 0615.cpt@vanoord.com m Tel: +31888263830	

Fisheries Liaison Contact

Specialist Marine Consultants is the appointed Fisheries Liaison Coordinator and can be contacted as follows:

Simon Prince – Fisheries Liaison Co-ordinator
 Specialist Marine Consultants Ltd
 +44 (0) 7920 273866
 Email: simonp@smchse.com

John Armstrong- Fishing Industry Representative
 Specialist Marine Consultants Ltd
 +44 (0) 7498 318694
 Email: smcflo@smchse.com
